


Construction Site Monitoring System

AI-powered safety, productivity
and progress management

Single-site scope, implementation approach
and commercial framework

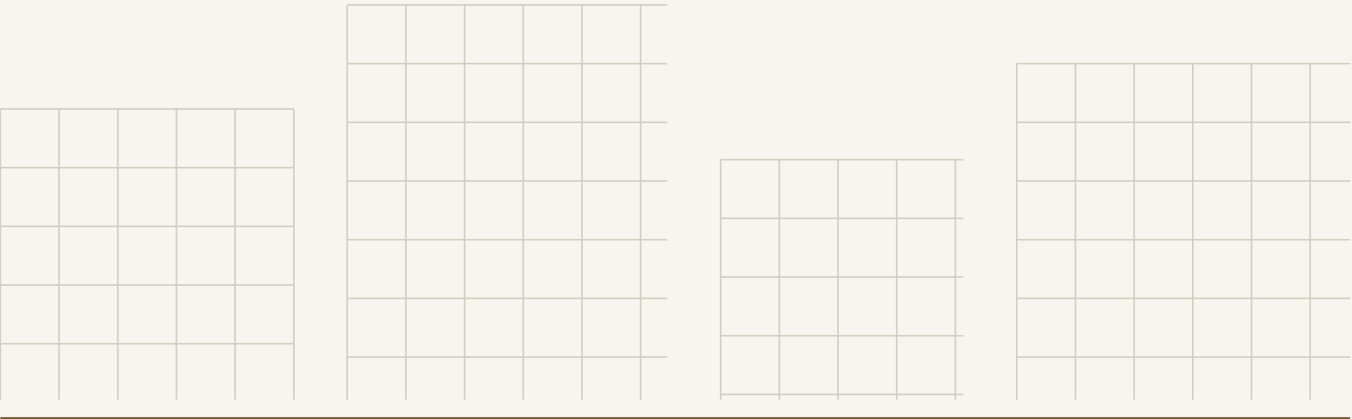

Presented by K Konsulting

Technology & development partner: SRS Logics

01 / EXECUTIVE OVERVIEW

Proposal overview

Camera-based monitoring for one construction site.

K Konsulting presents this single-site proposal to its client, with SRS Logics as the technology and development partner. The scope covers camera-based safety monitoring, site activity, progress records and management reports. As the client currently has no hardware, equipment and installation are budgeted separately. The delivery matrix on page 14 defines the fee boundary. Additional sites and optional extensions require written approval.

Safety monitoring

Flag possible PPE violations and restricted-zone entries. Safety officers can review the footage and record the action taken.

Site activity

Record visible workforce presence, vehicle movements, equipment activity and agreed material-handling events.

Progress records

Keep dated images from fixed cameras so project teams can compare changes and review visible milestones.

Management reporting

Bring site reports, open incidents and camera status into one dashboard, with access restricted by role and project.

CONTENTS

Core monitoring & operations	03	Scope and fee matrix	14
Progress, reports & integrations	04	Milestones & commercial authority	15
Architecture & operating workflow	05-06	POC decision & AI acceptance	16
Roadmap & POC testing	07-08	Warranty, AMC & support	17
Technical limits & security	09-10	Sizing, procurement & site readiness	18
Deliverables & responsibilities	11	Ownership, training & handover	19
Development, setup & running costs	12-13	Contract controls & approvals	20

02 / PLATFORM SCOPE

Core monitoring & operations

The platform vision below is governed by the included, POC-gated and optional scope on page 14.

Site setup and zones

Configure the project and its site, buildings, towers, floors, gates, zones and camera locations. Show workforce observations, safety events, incidents and camera health for this site.

Live cameras & infrastructure health

Site/zone listings, live view, camera grids, search, full-screen access and event timelines. Track offline cameras, unavailable streams, interrupted connections and processing failures.

Workforce & presence

Person detection, visible counts, zone occupancy, movement and entry/exit observations. Working-hour estimates and named attendance depend on approved identification integrations.

Safety, PPE & restricted zones

Configure helmet/vest detection and visible PPE where practical; zone intrusion and unsafe-area rules. Congestion, person-down and smoke/fire indicators require separate feasibility validation.

Vehicles, gates & machinery

Detect and classify selected cars, trucks, dumpers, mixers, excavators, loaders and cranes. Gate movements and selected classes are POC-gated. ANPR is a separately quoted extension.

Materials & equipment activity

POC-gated observation of loading/unloading, arrivals and storage-area movement, plus visible equipment presence and activity. Exact inventory and telematics are separately quoted.

03 / INTELLIGENCE & ACCESS

Progress, reporting & connected systems

Basic visual records and standard reports are included; advanced AI and connectors are optional.

Visual construction progress

Scheduled fixed-camera captures, daily/weekly images, before-and-after comparisons, timeline views, milestone evidence and time-lapse. Advanced change detection, structural-stage, floor-level or area-completion indicators require clearly defined, measurable use cases.

Analytics & daily reports

Workforce observations, peak occupancy, zone activity, PPE and incident trends, vehicle movements, equipment activity, camera health and progress summaries. Filter by project, site, camera, zone, date, event type and severity; standard CSV exports and a printable daily summary are included. The report field list is approved before development.

Web, PWA & role access

Responsive dashboard and mobile/PWA access for cameras where supported, alerts, incident review, progress and reports. Roles: super administrator, management, project manager, site manager, safety officer, security and read-only viewer.

OPTIONAL INTEGRATIONS

Operational need	Potential integration
Identity & access	RFID, QR/ID cards, approved biometric attendance and access control
Materials & inventory	QR/barcodes, RFID, weighbridges, gate-pass, inventory and ERP systems
Equipment & site context	GPS, equipment telematics, IoT and environmental sensors
Project coordination	Project-management systems, BIM and compatible video-management APIs

Productivity indicators describe visible site activity. They require context and should support management review rather than determine individual performance or certified project completion.

04 / REFERENCE ARCHITECTURE

System architecture

The budget assumes cloud AI with local recording. A different design requires an approved re-quote.

01 New IP cameras & local NVR

New equipment for the client site. Continuous footage is recorded locally; selected streams feed cloud AI.

02 Cloud AI processing - budget basis

Secure stream ingestion, selected AI checks and event rules. Camera resolution, analyzed frame rate, GPU capacity and upload bandwidth are approved through the sizing sheet.

Alternative: edge / hybrid processing

On-site inference may be selected after assessment. An edge AI device is not included in the current hardware allowance; equipment, software impact and revised costs need written approval.

EVENTS + METADATA + REQUIRED MEDIA

03 Central platform & event services

Python APIs and business logic; rules validation, incident ownership, notifications, reporting and integrations. Separate structured records from media evidence storage.

04 Data & evidence

Relational database; snapshots, available event clips and progress images in object/media storage.

05 Web / PWA access

Role-scoped live views, alerts, incident review, site analytics and reports.

Sizing the system

One site and up to eight camera connections in the software baseline. Processing workload, storage, upload bandwidth and retention must pass the sizing approval on page 18.

Technology direction: responsive HTML/CSS/JavaScript frontend, Python services, OpenCV and task-specific detection models. Frameworks, model licenses and infrastructure providers: To Be Finalized.

05 / OPERATING WORKFLOW

Alerts and incident handling

Each alert should reach a named person and retain a record of the response.

01

Observe

Read the configured camera stream and identify a supported object or event.

02

Validate

Apply zones, schedules, confidence thresholds and event rules; suppress duplicate alerts where configured.

03

Preserve

Create an event with site, zone, camera, timestamp, event type and priority. Store a snapshot and available clip/reference.

04

Notify & assign

Route to the responsible safety, site or security team. Track severity, ownership and acknowledgement.

05

Review & resolve

Review evidence, confirm or dismiss the event, document action and comments, and close the incident.

06

Review & report

Keep the action history and include confirmed events in reports. Review recurring false alerts before changing rules or models.

Example: a possible missing helmet

Configured PPE event → safety officer review → site manager escalation if unresolved → management escalation for defined critical conditions.

Dashboard alerts and configured email are included. Client email credentials are required; provider charges are separate. SMS, WhatsApp and other connectors are optional. The client staffs site response; no 24-hour human monitoring team is included.

06 / RECOMMENDED ROADMAP

Implementation sequence

We recommend the following sequence. Dates and durations are To Be Finalized.

- | | | |
|----|--|-------------------------------------|
| 01 | Technical discovery / site survey
Agree use cases, locations, stakeholders and constraints. | Approved discovery scope |
| 02 | Camera / network assessment
Plan camera coverage, stream requirements, lighting, power and connectivity. | Readiness and remediation plan |
| 03 | Proof of concept
Evaluate selected use cases with representative site footage and cameras. | Documented POC results |
| 04 | AI accuracy validation
Measure errors and operational performance against agreed acceptance criteria. | Acceptance or further testing |
| 05 | Core platform
Build site/camera setup, role access, dashboard, validated AI events and incidents. | Platform review and acceptance |
| 06 | Pilot deployment
Operate at the selected site, train users and validate end-to-end workflows. | Pilot review and corrective actions |
| 07 | Site production deployment
Move the accepted pilot into routine use at this site; confirm monitoring and support. | Site-level acceptance |
| 08 | Optional AI / IoT integrations
Add ANPR, precise inventory, advanced progress AI and external connectors by approved change. | Acceptance of each added function |

Included and successful POC-gated modules are completed within the agreed delivery plan. Optional extensions and further sites require a change order. Dates remain To Be Finalized; the schedule and readiness dependencies are approved after discovery, before core development.

07 / PROOF OF CONCEPT

POC and acceptance testing

Start with one site, a selected camera set and a small number of agreed use cases.

Prioritize person detection, helmet/vest checks, restricted-zone events and selected vehicle detection. Confirm the final camera count, use cases and operating conditions during discovery. The POC establishes feasibility; the pilot validates the operational service with real users.

Validation area	Proposed method
Representative data	Sample day/night conditions, shifts, distances, occlusion, weather and normal/abnormal activity. Obtain authorized, labeled examples.
Independent evaluation	Separate model tuning material from held-out evaluation footage. Report results by use case, camera and operating condition.
Detection quality	Measure precision (correct alerts), recall (events found), missed events and false alerts per camera-hour. Document count error where relevant.
Operational performance	Measure end-to-end alert latency, stream availability, processing capacity, evidence retrieval and notification delivery.
User acceptance	Test alert assignment, review, escalation, closure, reporting and camera outages with nominated site users.

Acceptance criteria

The signed acceptance sheet on page 16 fixes targets, footage, sample size, test duration, operating conditions and approvers before testing.

Decision after testing

Use the page 16 go/no-go process. An unsupported function cannot be silently removed or replaced; scope and fee impacts require written agreement.

08 / ASSUMPTIONS & LIMITATIONS

Assumptions and technical limits

The following conditions affect what can be delivered and how results should be used.

Area	Boundary / project assumption
Camera visibility	Resolution, angle, mounting height, distance, glare, low light, rain, dust, obstruction and motion affect detection. Blind spots remain outside coverage.
People & attendance	Visible counts are observations, not a unique site headcount. Occlusion and cross-camera duplication can affect counts. Formal named attendance needs reliable identification.
PPE & critical safety	Only visually discernible PPE can be assessed. Small items may be unsuitable. Fall/person-down and smoke/fire indicators need separate validation and human review.
Vehicles & equipment	ANPR depends on plate visibility, lighting, motion and gate geometry. Visual movement is not engine run-time, fuel use, diagnostics or precise GPS location.
Materials & progress	Video alone does not establish exact stock quantity, weight, hidden work quality or certified completion. Inventory, weighbridge, schedule or BIM data may be required.
Infrastructure & availability	New cameras and network equipment are required. Client arranges site access, power and internet readiness. Outages can interrupt cloud alerts; buffering/recovery must be designed and tested.
Model maintenance	No universal accuracy guarantee. Changing cameras, site stages, PPE or equipment can require revalidation. Routine tuning within the accepted baseline is covered by AMC; new datasets or model training require a change order.

Site safety responsibilities

AI supports review and response. It does not replace supervision, mandated safety controls or dedicated fire and life-safety systems.

09 / PRIVACY & SECURITY

Privacy and security

These controls will be agreed with the client before production deployment.

Purpose & authority

The client approves lawful monitoring purposes, site notices and authorized data use. K Konsulting coordinates these decisions. Identity or biometric integrations need separate assessment and authorization.

Access & accountability

The client names access approvers. SRS Logics receives only approved, necessary technical access; K Konsulting has no default footage access. Use role restrictions, admin MFA and access/export audit logs.

Secure architecture

Require HTTPS/TLS for application and cloud links, encrypted cloud storage/backups and protected secrets. Isolate cameras; use an approved secure gateway/VPN for legacy streams. Keep camera ports off the public internet.

Retention & minimization

The client approves storage region and retention by data type before provisioning. Limit transfer to required data; configure deletion, export, backup and incident-preservation rules. No reuse for unrelated model training without authorization.

Human review & responsible use

Retain evidence for authorized review, allow false-event dismissal and capture corrections. Avoid unsupported conclusions about individuals from activity signals; document model limits for users.

Operational resilience

SRS Logics configures agreed software backup, logging and recovery checks. The client/vendor maintains power, internet and equipment. Name incident contacts and approve notification, recovery and restore-test targets before go-live.

Before live personal data is used, the parties sign data-processing roles, security controls and incident/offboarding procedures. Applicable Indian data-protection requirements and commencement dates are checked for the deployment; compliance is not presumed from this proposal.

10 / DELIVERY & OWNERSHIP

Deliverables and responsibilities

The final statement of work will confirm the deliverables for each approved stage.

Stage	Expected deliverables
Discovery & assessment	Requirements and prioritized use cases; site/camera inventory; coverage and network assessment; readiness actions; proposed deployment architecture.
POC & validation	Configured POC; labeled evaluation approach; measured AI and infrastructure results; limitations register; recommendation on which functions to proceed with.
Core & pilot	Responsive web/PWA platform; role and site setup; compatible cameras; validated AI modules; alerts, incidents, evidence, camera health and agreed reports.
Deployment & handover	Accepted single-site configuration; agreed integrations; deployment/configuration documentation; user/admin guidance; training and operational handover.
Advanced scope	Separately quoted ANPR, precise inventory, advanced progress AI, named attendance, ERP/BIM, GPS, sensors and equipment telematics. Basic POC-gated observation remains within page 14.

WORKING RESPONSIBILITIES

Party	Role and responsibilities
K Konsulting	Client-facing consultancy: consolidates requirements, coordinates client approvals and escalations, and maintains the agreed decision record. Billing authority is finalized separately.
SRS Logics	Technology and development partner: solution design, agreed software and AI configuration, integrations, testing, deployment assistance, documentation and training.
Client team	Nominate owners and reviewers; provide authorized site, camera, network and data access; coordinate hardware installation, workforce communication and acceptance feedback.

Detailed scope, sign-off authority, support, procurement, ownership and handover terms are set out on pages 14-20. These schedules form part of the proposed statement of work.

11 / COMMERCIAL PROPOSAL

Development in three payments

One site. Eight cameras assumed. Payments linked to the agreed delivery milestones.

DEVELOPMENT AND TESTING

Total fee: Rs. 6,60,000

The fee covers the page 14 baseline. Payments follow the measurable milestones on page 15.

At contract signing**Rs. 66,000**

10% of development fee

After development**Rs. 2,97,000**

45% of development fee

After handover**Rs. 2,97,000**

45% of development fee

Hardware, installation, monthly services and annual maintenance are separate expenses, detailed below and on page 13. The signing payment covers development only. Applicable taxes are additional.

SITE SETUP - A SEPARATE, ONE-TIME EXPENSE

Item	Budget allowance
IP cameras - eight units	Rs. 40,000-64,000
Recording equipment and surveillance storage	Rs. 25,000-40,000
Network switches, routers and UPS	Rs. 20,000-35,000
Cabling, mounting, installation and configuration	Rs. 20,000-40,000
Site setup allowance - total	Rs. 1,05,000-1,79,000

Confirm the site requirements first, then agree the equipment quotation and procurement terms before ordering. The amounts above are budget allowances; final costs depend on the survey and supplier quotations.

12 / OPERATING COSTS & TERMS

Services to run the site

Monthly operating services and annual maintenance are separate from development.

MONTHLY SERVICE ALLOWANCE

Service	Monthly allowance
AI processing, hosting, database and event storage	Rs. 35,000-50,000
Site internet connection	Rs. 1,000-3,000
Total per month - one site	Rs. 36,000-53,000

Budget Rs. 36,000-53,000 per month, separate from development, site setup and AMC. Actual charges depend on capacity and usage. Billing commencement will be agreed before provisioning. Applicable taxes are additional.

ANNUAL MAINTENANCE CONTRACT (AMC)

Rs. 1,18,800 / year

18% of development fee

Calculated at 18% of Rs. 6,60,000, excluding applicable taxes. Defined coverage and exclusions are on page 17. AMC begins after the agreed defect-warranty period unless a separate start is signed. Billing and service-hour fields are finalized before signing.

BASIS OF ESTIMATE

Cameras and coverage

The client currently has no hardware. Eight cameras is a budget assumption. The site survey will confirm coverage, equipment specifications, cable routes and installation needs.

Cloud processing

The allowance is for cloud AI and application services, with reduced analysis frame rates and local continuous recording. The page 18 sizing sheet must confirm capacity, retention and provider charges before purchase.

ADDITIONAL ITEMS, IF REQUIRED

Edge AI equipment, dedicated ANPR cameras, extensive outdoor cabling, poles/civil work and optional connectors are outside these allowances. Baseline discovery, initial labeling and tuning are included as defined on page 14; additional work needs an approved change order.

CONTRACT AND DELIVERY TERMS

No supplier order or recurring service increase is placed without approval. Acceptance and payment rules: page 15. Required contract decisions, delay handling and change control: page 20. Unresolved signing fields must be closed before execution.

13 / SCOPE AND FEE BOUNDARY

What the development fee includes

This matrix governs the Rs. 6,60,000 baseline and takes precedence over capability summaries.

Included: delivered within the fee. POC-gated: included in the fee if the agreed validation passes. Optional: separately priced and authorized; no automatic inclusion.

Work package	Status	Delivery boundary
Discovery and POC	Included	One-site discovery/survey and assessment; baseline data preparation and initial labeling, configuration and tuning; one agreed POC campaign and one correction/retest cycle. Scope and work-package values are approved before work starts.
Core platform	Included	One site and up to eight camera connections; zones, roles, live views, camera health, incident review/history, dashboard/email alerts and PWA access. Standard daily summary, safety/camera-health reports and CSV exports.
People and safety AI	POC-gated	Person detection, visible counts, helmet/vest checks and restricted-zone rules, only for the cameras, PPE classes and conditions approved in the acceptance sheet. No named attendance or safety guarantee.
Vehicle, machinery and material activity	POC-gated	Selected vehicle/machinery classes, gate movements, visible activity and selected loading/unloading or material-movement events. Exact stock, engine metrics and number-plate recognition are not included.
Visual progress and handover	Included	Dated snapshots, fixed-view comparison, time-lapse, manually reviewed milestone records; pilot, production configuration, source/documentation package and the training on page 19.
Advanced extensions	Optional	ANPR; named/biometric attendance; fall/person-down or smoke/fire AI; precise inventory; automated progress measurement; RFID/GPS/IoT, ERP/BIM and telematics; SMS/WhatsApp, native mobile apps and additional sites.

BASELINE CONTROL

Before signing, record user/viewer limits, standard report fields and baseline use cases. The POC camera subset, sizing and acceptance values are finalized after discovery at the gates on pages 16 and 18. Additional datasets, training cycles, reports, cameras or connectors require a priced change order. A failed POC-gated item follows page 16; it is never silently omitted.

14 / COMMERCIAL AUTHORITY & ACCEPTANCE

Milestones with clear sign-off

The agreed payment split is 10% / 45% / 45%; the fee is separate from equipment and services.

BEFORE THE AGREEMENT IS SIGNED

Client legal name/site address, contracting entity, invoice issuer, payment recipient and authorized signatories: To Be Finalized before signing. K Konsulting coordinates client communication; SRS Logics provides technical evidence. Neither role alone establishes authority to bind the client or collect payment. Any K Konsulting/SRS Logics agreement must align with the client-facing obligations.

Milestone / payment	Evidence required for release
Contract signing Rs. 66,000 / 10%	Executed agreement and baseline scope; named commercial and technical approvers; agreed work-package allocation, POC approval process, payment due period and supplier-purchase authority. The signing amount is the development advance only.
After development Rs. 2,97,000 / 45%	Integrated platform and accepted AI functions demonstrated against the approved requirements and test sheet, with functioning camera integration. Development acceptance is signed by the client-authorized approver. Pilot production handover and training remain a distinct stage.
After handover Rs. 2,97,000 / 45%	Accepted pilot/production configuration; completed handover checklist, source and licensed model/configuration delivery, approved account access, training and backup/restore evidence. The client-authorized approver signs handover; the final invoice is then raised.

REVIEW, DEFECTS AND INVOICE TIMING

The review period, invoice due period and escalation contacts are To Be Finalized before signing. The client accepts in writing or gives one consolidated defect list tied to agreed criteria. Material defects are corrected and retested; minor items may remain only on a mutually signed completion list. Silence is not automatic acceptance. Unresolved review delays follow page 20; undisputed invoices remain payable within the agreed period.

15 / POC GATE & ACCEPTANCE REGISTER

Validate before committing the rollout

POC hardware, footage access and evaluation criteria are approved before testing begins.

Validation group	Measures to record	Target / sign-off
People, PPE and zones	Per-use-case precision, recall, false alerts per camera-hour and visible-count error; camera position, distance, occlusion, day/night conditions and PPE classes.	Targets: To Be Finalized before POC; client technical approver.
Vehicles and material activity	Selected object/event classes, movement direction, false/missed events, count error and permitted gate/yard conditions. No inference of exact inventory or engine metrics.	Targets: To Be Finalized before POC; client technical approver.
Operational service	Analyzed streams/frame rate, alert latency, stream availability, event retention/retrieval, email delivery, outage behavior and backup/restore test.	Targets fixed before POC and rechecked at pilot; client IT/site approver.
Evaluation record	Labeled sample size, footage provenance, test duration, independent held-out footage, model/configuration version and per-camera results. SRS prepares evidence; K Konsulting coordinates review.	Names, test dates and thresholds are signed before evaluation.

GATE DECISION AND FEE TREATMENT

Pass: sign the accepted use cases and release core development. Correct: complete the included correction/retest cycle within the signed POC plan. Fail or defer: stop the affected scope; agree revised deliverables, price and schedule in writing, or close the engagement. Further paid testing requires prior approval. No unsupported item is silently substituted and the unchanged full fee is not automatically payable for a reduced scope.

IF THE ENGAGEMENT STOPS AT POC

Reconcile completed, agreed work against the work-package values fixed before signing, plus separately authorized non-cancellable supplier commitments. Refund or credit any unused advance after reconciliation; provide the completed POC findings. No automatic forfeiture of the signing advance or charge for unperformed development is proposed.

AFTER DEPLOYMENT

Maintain an approved camera/model baseline and a log of false alerts and changes. SRS Logics reviews reported degradation under the agreed support plan; the client supplies authorized examples. New site conditions are revalidated before relying on changed AI behavior. Review frequency and thresholds are fixed before go-live.

16 / WARRANTY & ANNUAL MAINTENANCE

A defined maintenance service

AMC: Rs. 1,18,800 per year, equal to 18% of the Rs. 6,60,000 development fee; taxes additional.

DEFECT WARRANTY AND AMC COMMENCEMENT

The development fee includes correction of reproducible departures from the accepted specification during the agreed defect-warranty period, starting at signed handover. Warranty duration is To Be Finalized before signing. AMC starts after that period unless a different start is expressly signed. Warranty and AMC charges must not overlap for the same covered service.

Coverage	Service boundary
Included in AMC	Remote incident diagnosis, fixes to accepted software, applicable security/dependency patches, routine threshold/zone tuning within the accepted baseline, and software-side camera reconnection assistance.
Platform operations	Agreed application/backup health checks, restore-test coordination, configuration advice and escalation to the hosting provider, where authorized access is supplied. Cloud subscriptions, storage and provider usage are billed separately.
Separately quoted	New features/classes, additional cameras/sites, replacement models, new training datasets, substantial retraining/revalidation, hardware repairs, network/civil work, travel and onsite attendance.
Billing and renewal	Annual fee applies to the current baseline. Billing frequency, due date, service hours and support contacts are finalized before signing. Renewal and any revised baseline/fee require written confirmation; no automatic price increase is assumed.

Priority	Example	Response / recovery
P1 - critical	System unavailable or widespread failure of accepted alert delivery.	Acknowledgement and workaround/recovery targets: To Be Finalized before signing.
P2 - significant	A camera or core workflow is impaired; a usable workaround exists.	Targets: To Be Finalized before signing; measured during agreed service hours.
P3 - routine	Minor defect, configuration question or scheduled maintenance.	Response and scheduling targets: To Be Finalized before signing.

Acknowledgement is distinct from restoration or permanent resolution. The client supplies site safety/security personnel and an escalation roster. No 24-hour staffed monitoring, hardware warranty or guaranteed prevention of incidents is included.

17 / INFRASTRUCTURE & PROCUREMENT

Approve the site before buying

Current allowances assume cloud AI and local continuous recording; they are not supplier quotations.

Sizing item	Approval required before purchase / provisioning
Site and camera baseline	One site; up to eight software camera connections. Final camera coverage plan, POC subset, physical locations and simultaneous analyzed streams are approved during discovery.
Camera and recording	Resolution, lenses, low-light suitability, codec, stream compatibility, analysis frame rate, recording bitrate, NVR channels and surveillance storage capacity: To Be Finalized in the equipment list.
Network and power	Measured internet upload, stream bandwidth, router/switch ports, network isolation, cable lengths, power and UPS needs, outage/reconnection behavior: To Be Finalized after assessment.
AI and cloud capacity	Model workload, operating hours, GPU/CPU/RAM, simultaneous viewers, media transfer, hosting region and provider charges: To Be Finalized and checked by POC. No unlimited processing/storage is implied.
Retention and recovery	Separate periods and volumes for raw video, event clips, images, logs and backups; restore objectives and test frequency: To Be Finalized before provisioning.
Alternative architecture	An edge inference device is not in the Rs. 1,05,000-1,79,000 hardware allowance. If edge/hybrid is selected, revise the equipment list, development impact and recurring estimate before authorization.

PROCUREMENT AND ONSITE OWNERSHIP

SRS Logics defines compatibility and software requirements; K Konsulting coordinates approvals. The client approves the supplier, equipment list, procurement payer and purchase terms. The named hardware vendor installs, tests and warrants equipment. The client/vendor handles cleaning, repositioning, cables, power and internet; SRS handles agreed software diagnosis. Vendor contacts, warranty terms and any site-visit/travel charges are approved before ordering.

POC PURCHASE AND SPENDING CONTROL

The client authorizes a minimum suitable POC camera/recording setup or rental before testing. Funding, ownership and reusable equipment are recorded separately; the Rs. 66,000 software advance does not fund hardware. Full-site procurement follows approved coverage and POC findings. Orders, paid subscriptions and usage increases above the approved budget require written authorization.

18 / OWNERSHIP & HANDOVER

An operable system at handover

Source delivery, account control, training and data return are recorded in a signed checklist.

SOURCE CODE AND LICENSING

Bespoke project source and deployment materials are included in handover. Ownership assignment or the project-use license is To Be Finalized before signing, together with any full-payment condition; source delivery alone is not an IP assignment. Pre-existing SRS Logics tools and third-party components retain their ownership. The signed license must permit the agreed operation and maintenance, identify any reuse/site limits, and list third-party obligations. No credentials are published with source.

Handover item	Required evidence
Application and AI	Frontend/backend source, database schema/migrations, inference and rules configuration, permitted model weights or acquisition instructions, dependency/license register and accepted version records.
Deployment and accounts	Installation/runbook, environment-variable template, backup/restore and troubleshooting instructions. Client-designated ownership/control of hosting, storage, domain and email accounts; least-privilege SRS access and credential rotation.
Acceptance records	Signed requirement/test results, accepted AI conditions, camera/network map, remaining agreed minor items, support contacts, warranty/AMC dates and service schedule.
Training	Two remote sessions are included: one for administrators and one for site operators. Supply user/admin guidance and an attendance record. Dates, duration and nominees are agreed in the delivery plan; additional sessions or onsite training need approval.
Client data and exit	Provide structured data in CSV and evidence media in agreed original formats, with configuration/reference information needed to interpret them. Data access, return, retention and deletion follow the signed processing schedule; extra migration work is separately agreed.

ACCESS AND OFFBOARDING

The client controls authorized use of site data and names access approvers. K Konsulting has no default access to footage; SRS Logics uses it only for agreed delivery/support. Before live processing, sign retention, incident contacts and an exit procedure: export, transfer accounts, revoke support access and confirm deletion subject to agreed retention or lawful preservation. Do not reuse client footage to train unrelated models without authorization.

19 / CONTRACT CONTROLS & APPROVALS

Decisions that close the agreement

The following controls are proposed for incorporation into the signed statement of work and agreement.

CHANGES, DEPENDENCIES AND THE DELIVERY CLOCK

Every change records scope, cost, schedule, acceptance and support impact; the authorized client representative approves it before work starts. Discovery, POC, development and deployment dates remain To Be Finalized. Approve the baseline schedule after discovery and before core development, with camera/data access, site readiness and client reviews as dependencies. Log delays promptly, agree revised dates in writing and escalate unreturned approvals; any pause affects only the agreed work and preserves agreed data/site safeguards.

CONFIDENTIALITY AND CANCELLATION

Each party protects confidential information, restricts disclosure to authorized delivery personnel and approved providers, and agrees return/deletion obligations. Termination grounds, notice/cure period and exit timing are finalized before signing. On closure, reconcile approved completed work and authorized supplier commitments against the agreed allocation; refund/credit unused advances. No unapproved cancellation charge or automatic forfeiture is introduced.

LIABILITY AND DISPUTE HANDLING

The agreement allocates responsibility for software defects, physical equipment, connectivity and operational response. AI limitations do not remove responsibility for agreed delivery or contractual duties. Liability limits, exclusions, mandatory-law exceptions, governing law, jurisdiction and dispute-escalation procedure are To Be Finalized before signing. No unlimited liability, insurance cover or performance guarantee is implied by the fee.

Gate	Fields that must be closed	Decision owners
Before signing	Client legal name/site address; contracting, invoicing and payment entity; signatories; validity; scope/work-package allocation; review/invoice periods; IP/license; warranty, AMC hours/targets; termination and liability terms.	Authorized representatives of the client, K Konsulting and SRS Logics, as applicable.
Before POC / orders	POC cameras, data authority, test conditions/sample/targets; approved equipment list, supplier, payer, purchase/rental and travel terms; agreed fee treatment if POC fails.	Client technical/commercial approvers, coordinated by K Konsulting; SRS technical lead.
Core, pilot and go-live	Before core: signed POC decision and delivery schedule. Before pilot: approved sizing/cost, reports/access and privacy/incident plans. Before go-live: accepted pilot. At handover: completed delivery/support checklist.	Client IT/site approvers and SRS technical lead; K Konsulting records approvals.

The scope matrix, accepted test sheets and approved changes govern delivery. The demo is illustrative; it does not add capabilities or AI guarantees. Unresolved signing fields must be completed before execution; later gate fields must be completed before that stage starts.
